

ID	Task Mode	Task Name	Duration	Start	2 Dec '24		9 Dec '24		16 Dec '24		23 Dec '24		30 Dec '24		6 Jan '25														
					S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T
1		<b>1-14173.00 KDC Advisory - HIGH Complexity</b>	<b>35 days</b>	<b>22/01/25</b>																									
2		<b>Bickerstaffe Rd RP4591</b>	<b>11 days</b>	<b>28/01/25</b>																									
3		Drone Survey	0 days	28/01/25																									
4		Design Parameters/Ground model	1 day	3/02/25																									
5		Retaining Wall Design	1 day	4/02/25																									
6		Review	1 day	5/02/25																									
7		Slope Stability	1 day	6/02/25																									
8		Design Report	1 day	7/02/25																									
9		Review	1 day	10/02/25																									
10		Draughting	5 days	4/02/25																									
11		Review	1 day	11/02/25																									
12		SOQ	1 day	11/02/25																									
13		Issue to Client	0 days	11/02/25																									
14		<b>Bickerstaffe Rd RP6150</b>	<b>11 days</b>	<b>28/01/25</b>																									
15		Drone Survey	0 days	28/01/25																									
16		H&S Documentation	1 day	28/01/25																									
17		Service Locate	1 day	3/02/25																									
18		Scala testing	1 day	3/02/25																									
19		Design Parameters/Ground model	1 day	4/02/25																									
20		Retaining Wall Design	1 day	5/02/25																									
21		Review	1 day	6/02/25																									
22		Slope Stability	1 day	7/02/25																									
23		Design Report	1 day	10/02/25																									
24		Review	1 day	11/02/25																									
25		Draughting	5 days	4/02/25																									
26		Review	1 day	11/02/25																									
27		SOQ	1 day	11/02/25																									
28		Issue to Client	0 days	11/02/25																									
29		<b>Tinopai Rd RP16190</b>	<b>12 days</b>	<b>22/01/25</b>																									
30		H&S Documentation	1 day	22/01/25																									
31		Service Locate	1 day	23/01/25																									
32		CPTS & Hand Augers	5 days	23/01/25																									
33		Design Parameters/Ground model	1 day	30/01/25																									
34		Retaining Wall Design	1 day	31/01/25																									
35		Review	1 day	3/02/25																									
36		Slope Stability	1 day	4/02/25																									
37		Design Report	1 day	5/02/25																									
38		Review	1 day	6/02/25																									

Project: KDC Programming Date: 24/01/25	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	2 Dec '24		9 Dec '24		16 Dec '24		23 Dec '24		30 Dec '24		6 Jan '25														
					S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T
39		Draughting	5 days	30/01/25																									
40		Review	1 day	6/02/25																									
41		SOQ	1 day	6/02/25																									
42		Issue to Client	0 days	6/02/25																									
43		<b>Golden Stairs Rd RP4828</b>	<b>12 days</b>	<b>28/01/25</b>																									
44		Drone Survey	0 days	28/01/25																									
45		H&S Documentation	1 day	28/01/25																									
46		Service Locate	1 day	3/02/25																									
47		Scala testing	1 day	4/02/25																									
48		Design Parameters/Ground model	1 day	5/02/25																									
49		Retaining Wall Design	1 day	6/02/25																									
50		Review	1 day	7/02/25																									
51		Slope Stability	1 day	10/02/25																									
52		Design Report	1 day	11/02/25																									
53		Review	1 day	12/02/25																									
54		Draughting	5 days	5/02/25																									
55		Review	1 day	12/02/25																									
56		SOQ	1 day	12/02/25																									
57		Issue to Client	0 days	12/02/25																									
58		<b>Murray Rd RP3500</b>	<b>30 days</b>	<b>29/01/25</b>																									
59		Drone Survey	0 days	29/01/25																									
60		H&S Documentation	1 day	29/01/25																									
61		Service Locate	1 day	4/02/25																									
62		3 x CPT's & 2 x BH's	14 days	5/02/25																									
63		GIR	4 days	25/02/25																									
64		Planning/Ecology Assessment	5 days	5/02/25																									
65		Pavement Design	5 days	25/02/25																									
66		Hydrology Assessment	7 days	5/02/25																									
67		Draft SMS Report	5 days	4/03/25																									
68		Review	1 day	11/03/25																									
69		Issue to Client	0 days	12/03/25																									
70		<b>Colville Rd RP140</b>	<b>16 days</b>	<b>29/01/25</b>																									
71		Drone Survey	0 days	29/01/25																									
72		H&S Documentation	1 day	29/01/25																									
73		Service Locate	1 day	4/02/25																									
74		CPTS & Hand Augers	5 days	5/02/25																									
75		Design Parameters/Ground model	1 day	12/02/25																									
76		Retaining Wall Design	1 day	13/02/25																									
77		Review	1 day	14/02/25																									
78		Slope Stability	1 day	17/02/25																									

Project: KDC Programming  
Date: 24/01/25

	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	2 Dec '24		9 Dec '24		16 Dec '24		23 Dec '24		30 Dec '24		6 Jan '25														
					S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T
79		Design Report	1 day	18/02/25																									
80		Review	1 day	19/02/25																									
81		Draughting	5 days	12/02/25																									
82		Review	1 day	19/02/25																									
83		SOQ	1 day	19/02/25																									
84		Issue to Client	0 days	19/02/25																									
85		<b>Tangowahine Valley Rd RP13670</b>	<b>16 days</b>	<b>30/01/25</b>																									
86		Drone Survey	0 days	30/01/25																									
87		H&S Documentation	1 day	3/02/25																									
88		Service Locate	1 day	5/02/25																									
89		CPTS & Hand Augers	5 days	6/02/25																									
90		Design Parameters/Ground model	1 day	13/02/25																									
91		Retaining Wall Design	1 day	14/02/25																									
92		Review	1 day	17/02/25																									
93		Slope Stability	1 day	18/02/25																									
94		Design Report	1 day	19/02/25																									
95		Review	1 day	20/02/25																									
96		Draughting	5 days	13/02/25																									
97		Review	1 day	20/02/25																									
98		SOQ	1 day	20/02/25																									
99		Issue to Client	0 days	20/02/25																									
100		<b>Maitahi Rd RP1636 (TBC PENDING WIND FARM PROJECT)</b>	<b>11 days</b>	<b>30/01/25</b>																									
101		Drone Survey	0 days	30/01/25																									
102		H&S Documentation	1 day	30/01/25																									
103		Service Locate	1 day	5/02/25																									
104		Scala testing	1 day	5/02/25																									
105		Design Parameters/Ground model	1 day	6/02/25																									
106		Retaining Wall Design	1 day	7/02/25																									
107		Review	1 day	10/02/25																									
108		Slope Stability	1 day	11/02/25																									
109		Design Report	1 day	12/02/25																									
110		Review	1 day	13/02/25																									
111		Draughting	5 days	6/02/25																									
112		Review	1 day	13/02/25																									
113		SOQ	1 day	13/02/25																									
114		Issue to Client	0 days	13/02/25																									
115		<b>Pahi Rd RP4036</b>	<b>15 days</b>	<b>31/01/25</b>																									
116		Drone Survey	0 days	31/01/25																									
117		H&S Documentation	1 day	31/01/25																									
118		Service Locate	1 day	6/02/25																									

Project: KDC Programming Date: 24/01/25	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	2 Dec '24		9 Dec '24		16 Dec '24		23 Dec '24		30 Dec '24		6 Jan '25														
					S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T
119		CPTS & Hand Augers	5 days	6/02/25																									
120		Design Parameters/Ground model	1 day	13/02/25																									
121		Retaining Wall Design	1 day	14/02/25																									
122		Review	1 day	17/02/25																									
123		Slope Stability	1 day	18/02/25																									
124		Design Report	1 day	19/02/25																									
125		Review	1 day	20/02/25																									
126		Draughting	5 days	13/02/25																									
127		Review	1 day	20/02/25																									
128		SOQ	1 day	20/02/25																									
129		Issue to Client	0 days	20/02/25																									
130		<b>Trounson Park RP3962</b>	<b>11 days</b>	<b>13/02/25</b>																									
131		Ecological/Arch Assessment	5 days	13/02/25																									
132		Design Parameters/Ground model	1 day	13/02/25																									
133		Retaining Wall Design	1 day	14/02/25																									
134		Review	1 day	17/02/25																									
135		Slope Stability	1 day	18/02/25																									
136		Design Report	1 day	19/02/25																									
137		Review	1 day	20/02/25																									
138		Draughting	5 days	20/02/25																									
139		Review	1 day	27/02/25																									
140		SOQ	1 day	27/02/25																									
141		Issue to Client	0 days	27/02/25																									
142		<b>Pukehuia Rd RP15773</b>	<b>12 days</b>	<b>31/01/25</b>																									
143		Drone Survey	0 days	31/01/25																									
144		H&S Documentation	1 day	31/01/25																									
145		Service Locate	1 day	6/02/25																									
146		Scala testing	1 day	7/02/25																									
147		Design Parameters/Ground model	1 day	10/02/25																									
148		Retaining Wall Design	1 day	11/02/25																									
149		Review	1 day	12/02/25																									
150		Slope Stability	1 day	13/02/25																									
151		Design Report	1 day	14/02/25																									
152		Review	1 day	17/02/25																									
153		Draughting	5 days	10/02/25																									
154		Review	1 day	17/02/25																									
155		SOQ	1 day	17/02/25																									
156		Issue to Client	0 days	17/02/25																									
157																													
158		<b>1-14173.00 KDC Advisory - MEDIUM Complexity</b>	<b>53 days?</b>	<b>1/12/24</b>																									

Project: KDC Programming Date: 24/01/25	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	2 Dec '24							9 Dec '24							16 Dec '24							23 Dec '24							30 Dec '24							6 Jan '25										
					S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T
159	→	<b>Whakapirau Rd RP7000</b>	28 days	16/12/24																																														
160	→	Drawings Issued to Client	0 days	16/12/24																																														
161	→	SOQ Issued to Client	0 days	17/12/24																																														
162	→	LRP's Issued to Client	0 days	23/01/25																																														
163	→	<b>Pahi Rd RP2708</b>	0 days	5/12/24																																														
164	→	Memo & Sketch Issued to Client	0 days	5/12/24																																														
165	→	<b>Tinopai Rd RP16190</b>	4 days	5/12/24																																														
166	→	Drawings Issued to Client	0 days	5/12/24																																														
167	→	SOQ Issued to Client	0 days	11/12/24																																														
168	→	<b>Murray Rd RP1650</b>	0 days	6/12/24																																														
169	→	Memo & Sketch Issued to Client	0 days	6/12/24																																														
170	→	<b>Bickerstaffe Rd RP7655</b>	0 days	10/12/24																																														
171	→	Memo & Sketch Issued to Client	0 days	10/12/24																																														
172	→	<b>Bickerstaffe Rd RP8850</b>	0 days	21/01/25																																														
173	→	Memo & Sketch Issued to Client	0 days	21/01/25																																														
174	→	<b>Bickerstaffe Rd RP9200</b>	32 days	10/12/24																																														
175	→	Drawings Issued to Client	0 days	10/12/24																																														
176	→	SOQ Issued to Client	0 days	11/12/24																																														
177	→	LRP's Issued to Client	0 days	23/01/25																																														
178	→	<b>Whakapirau Rd RP10000</b>	0 days	9/12/24																																														
179	→	Memo & Sketch Issued to Client	0 days	9/12/24																																														
180	→	<b>Houto Rd RP2270</b>	28 days	16/12/24																																														
181	→	Drawings Issued to Client	0 days	16/12/24																																														
182	→	SOQ Issued to Client	0 days	16/12/24																																														
183	→	LRP's Issued to Client	0 days	23/01/25																																														
184	→	<b>Houto Rd RP2800/2880</b>	31 days	11/12/24																																														
185	→	Drawings Issued to Client	0 days	11/12/24																																														
186	→	SOQ Issued to Client	0 days	16/12/24																																														
187	→	LRP's Issued to Client	0 days	23/01/25																																														
188	→	<b>Bob Taylor Rd RP567</b>	0 days	30/01/25																																														
189	→	Issued to Client	0 days	30/01/25																																														
190	→	LRPs Issued to Client	0 days	30/01/25																																														
191	→	<b>Colville Rd RP210</b>	5 days	30/01/25																																														
192	→	Service Locate	0 days	30/01/25																																														
193	→	Issued to Client	5 days	30/01/25																																														
194	→	<b>Mason Rd RP2086</b>	0 days	21/01/25																																														
195	→	Sketch Issued to Client	0 days	21/01/25																																														
196	→	<b>Mangarata Block Rd RP2300</b>	10 days	30/01/25																																														
197	→	Service Locate	0 days	30/01/25																																														
198	→	Issued to Client	10 days	30/01/25																																														
199	→	<b>Girls High School Rd RP1100 (TBC)</b>	1 day?	1/12/24																																														

- ◆ Whakapirau Rd RP10000
- ◆ Memo & Sketch Issued to Client
- ◆ Drawings Issued to Client
- ◆ SOQ Issued to Client
- ◆ Murray Rd RP1650
- ◆ Memo & Sketch Issued to Client
- ◆ 10/12
- ◆ Memo & Sketch Issued to Client

- ◆ Bickerstaffe Rd RP9200
- ◆ Drawings Issued to Client
- ◆ SOQ Issued to Client

- ◆ Whakapirau Rd RP10000
- ◆ Memo & Sketch Issued to Client

- ◆ Houto Rd RP2270
- ◆ Drawings Issued to Client
- ◆ SOQ Issued to Client


- ◆ Houto Rd RP2800/2880
- ◆ Drawings Issued to Client
- ◆ SOQ Issued to Client

Project: KDC Programming Date: 24/01/25	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	2 Dec '24		9 Dec '24							16 Dec '24							23 Dec '24							30 Dec '24							6 Jan '25								
					S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T
200		Drone Survey	1 day?	1/12/24																																							
201		Issued to Client	1 day?	2/12/24																																							

Project: KDC Programming  
Date: 24/01/25


	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

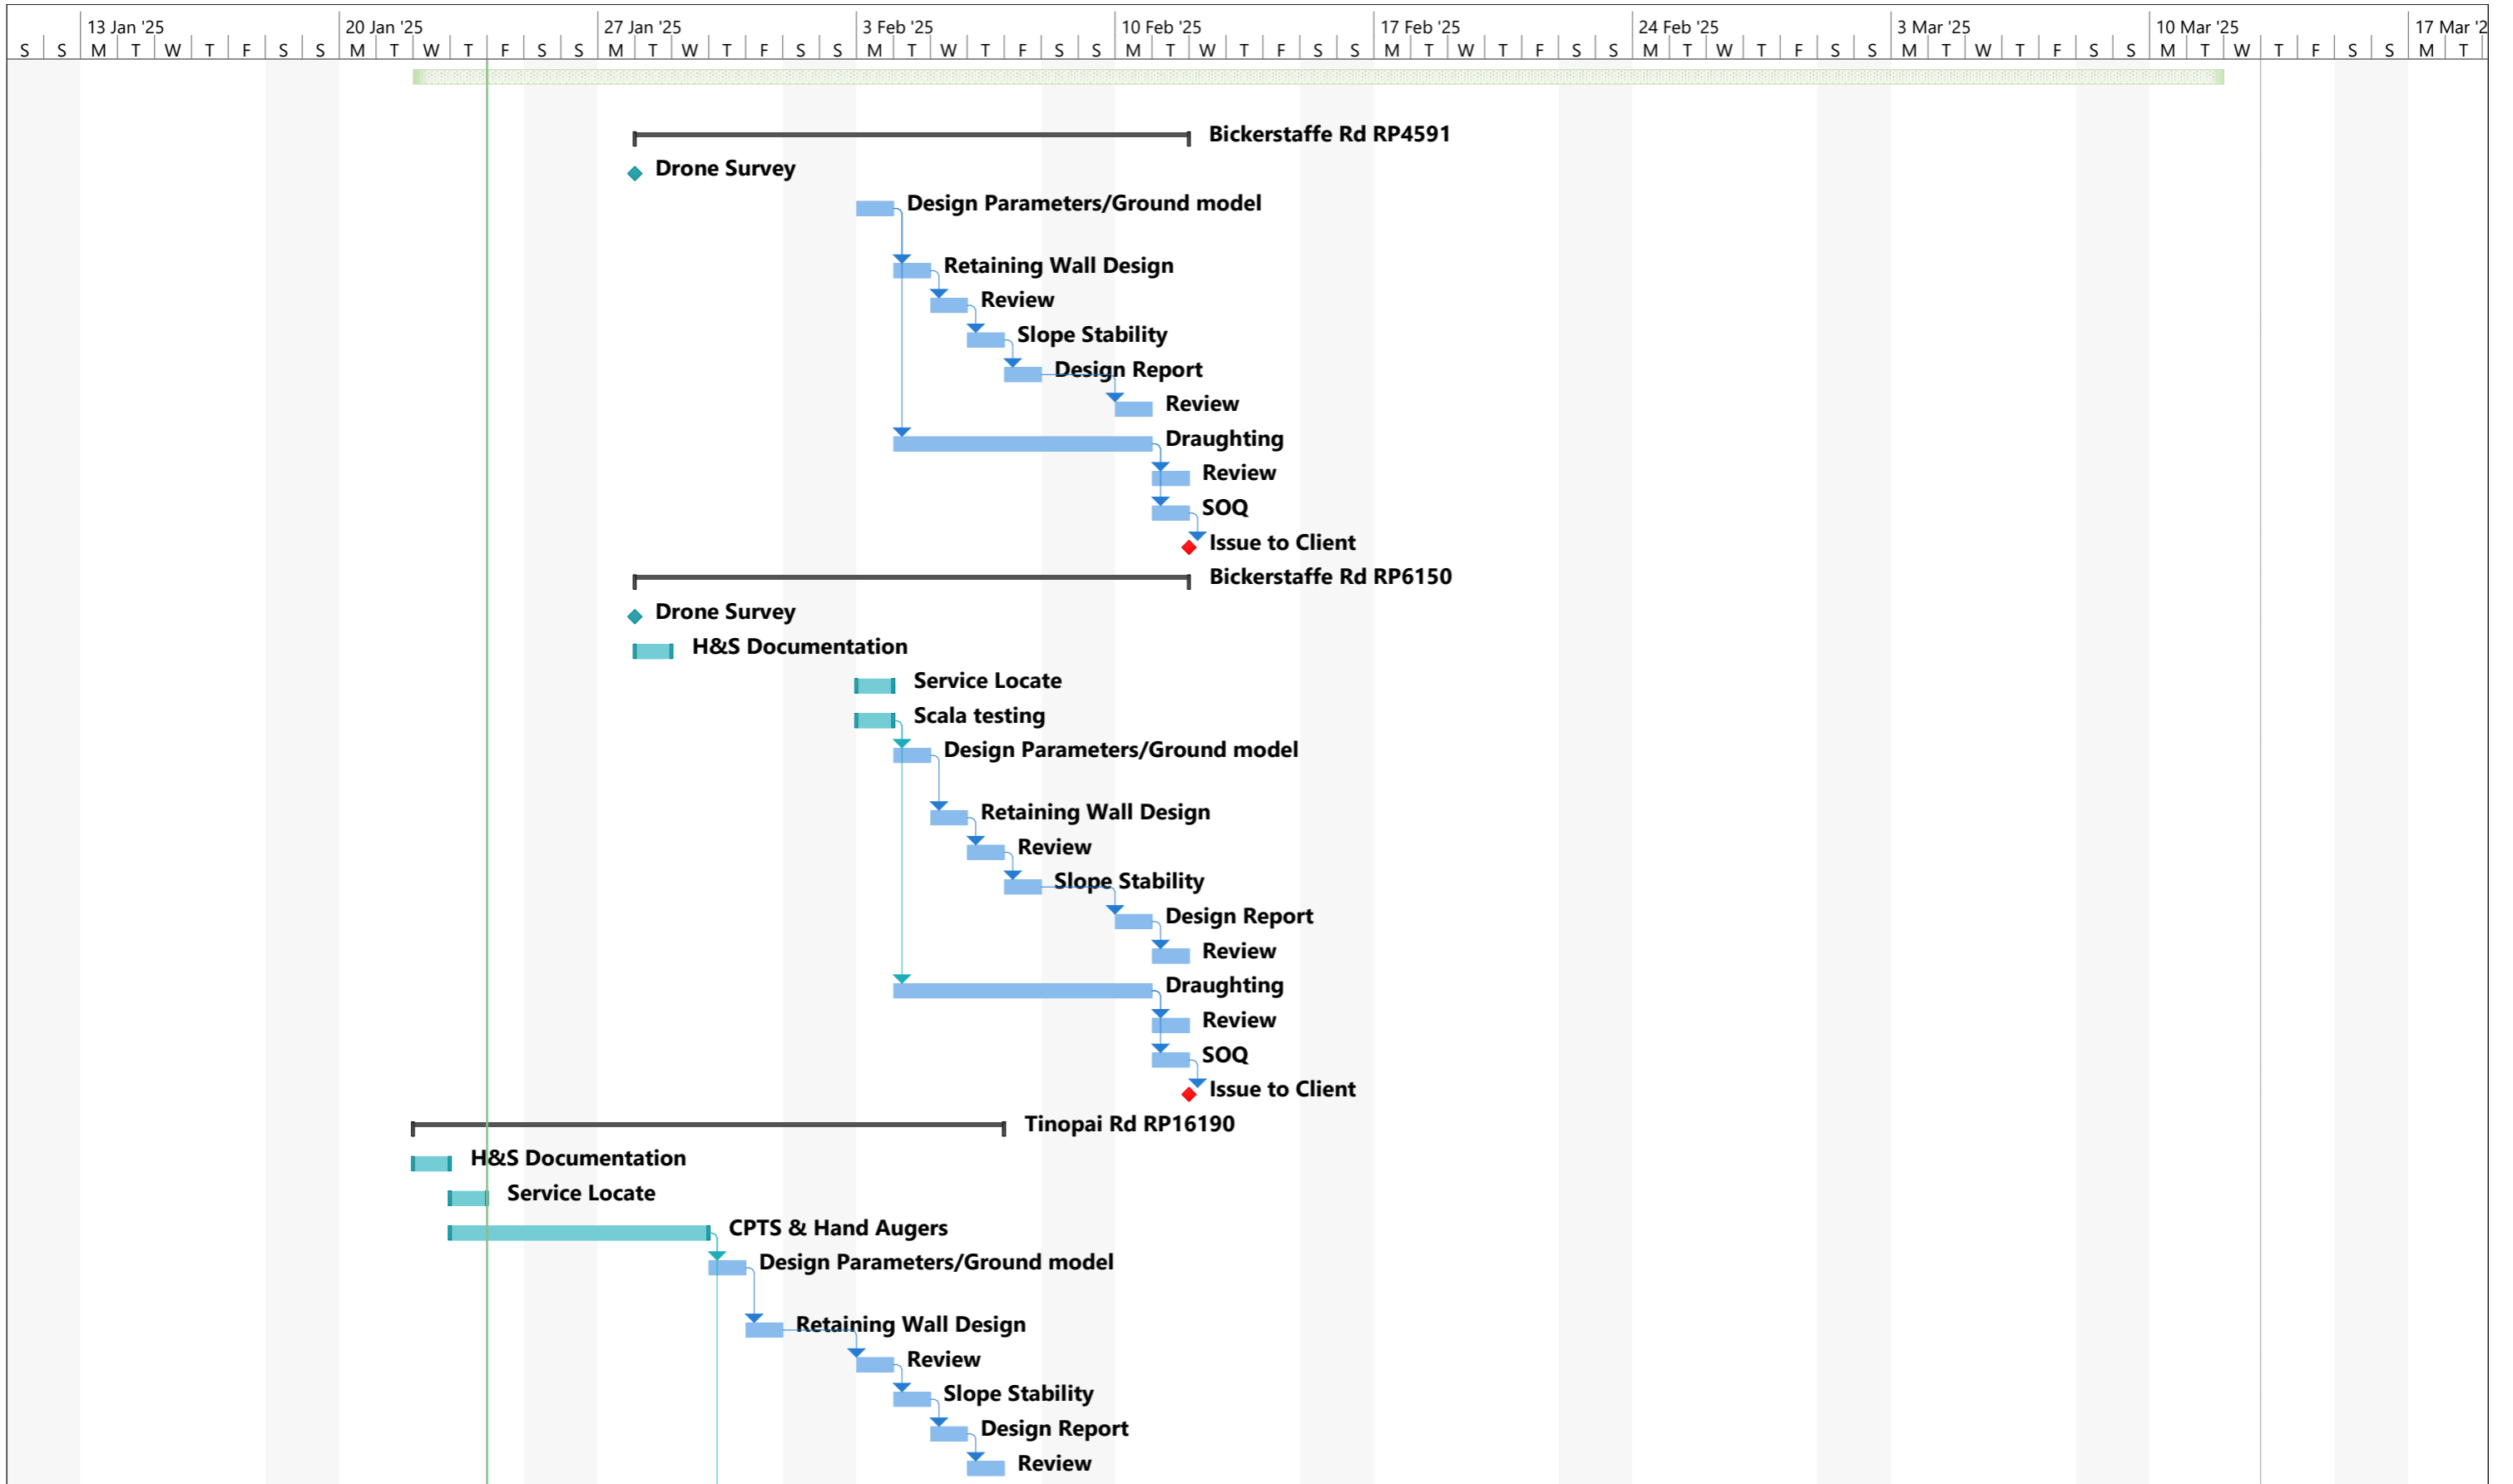

Project: KDC Programming  
Date: 24/01/25

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			




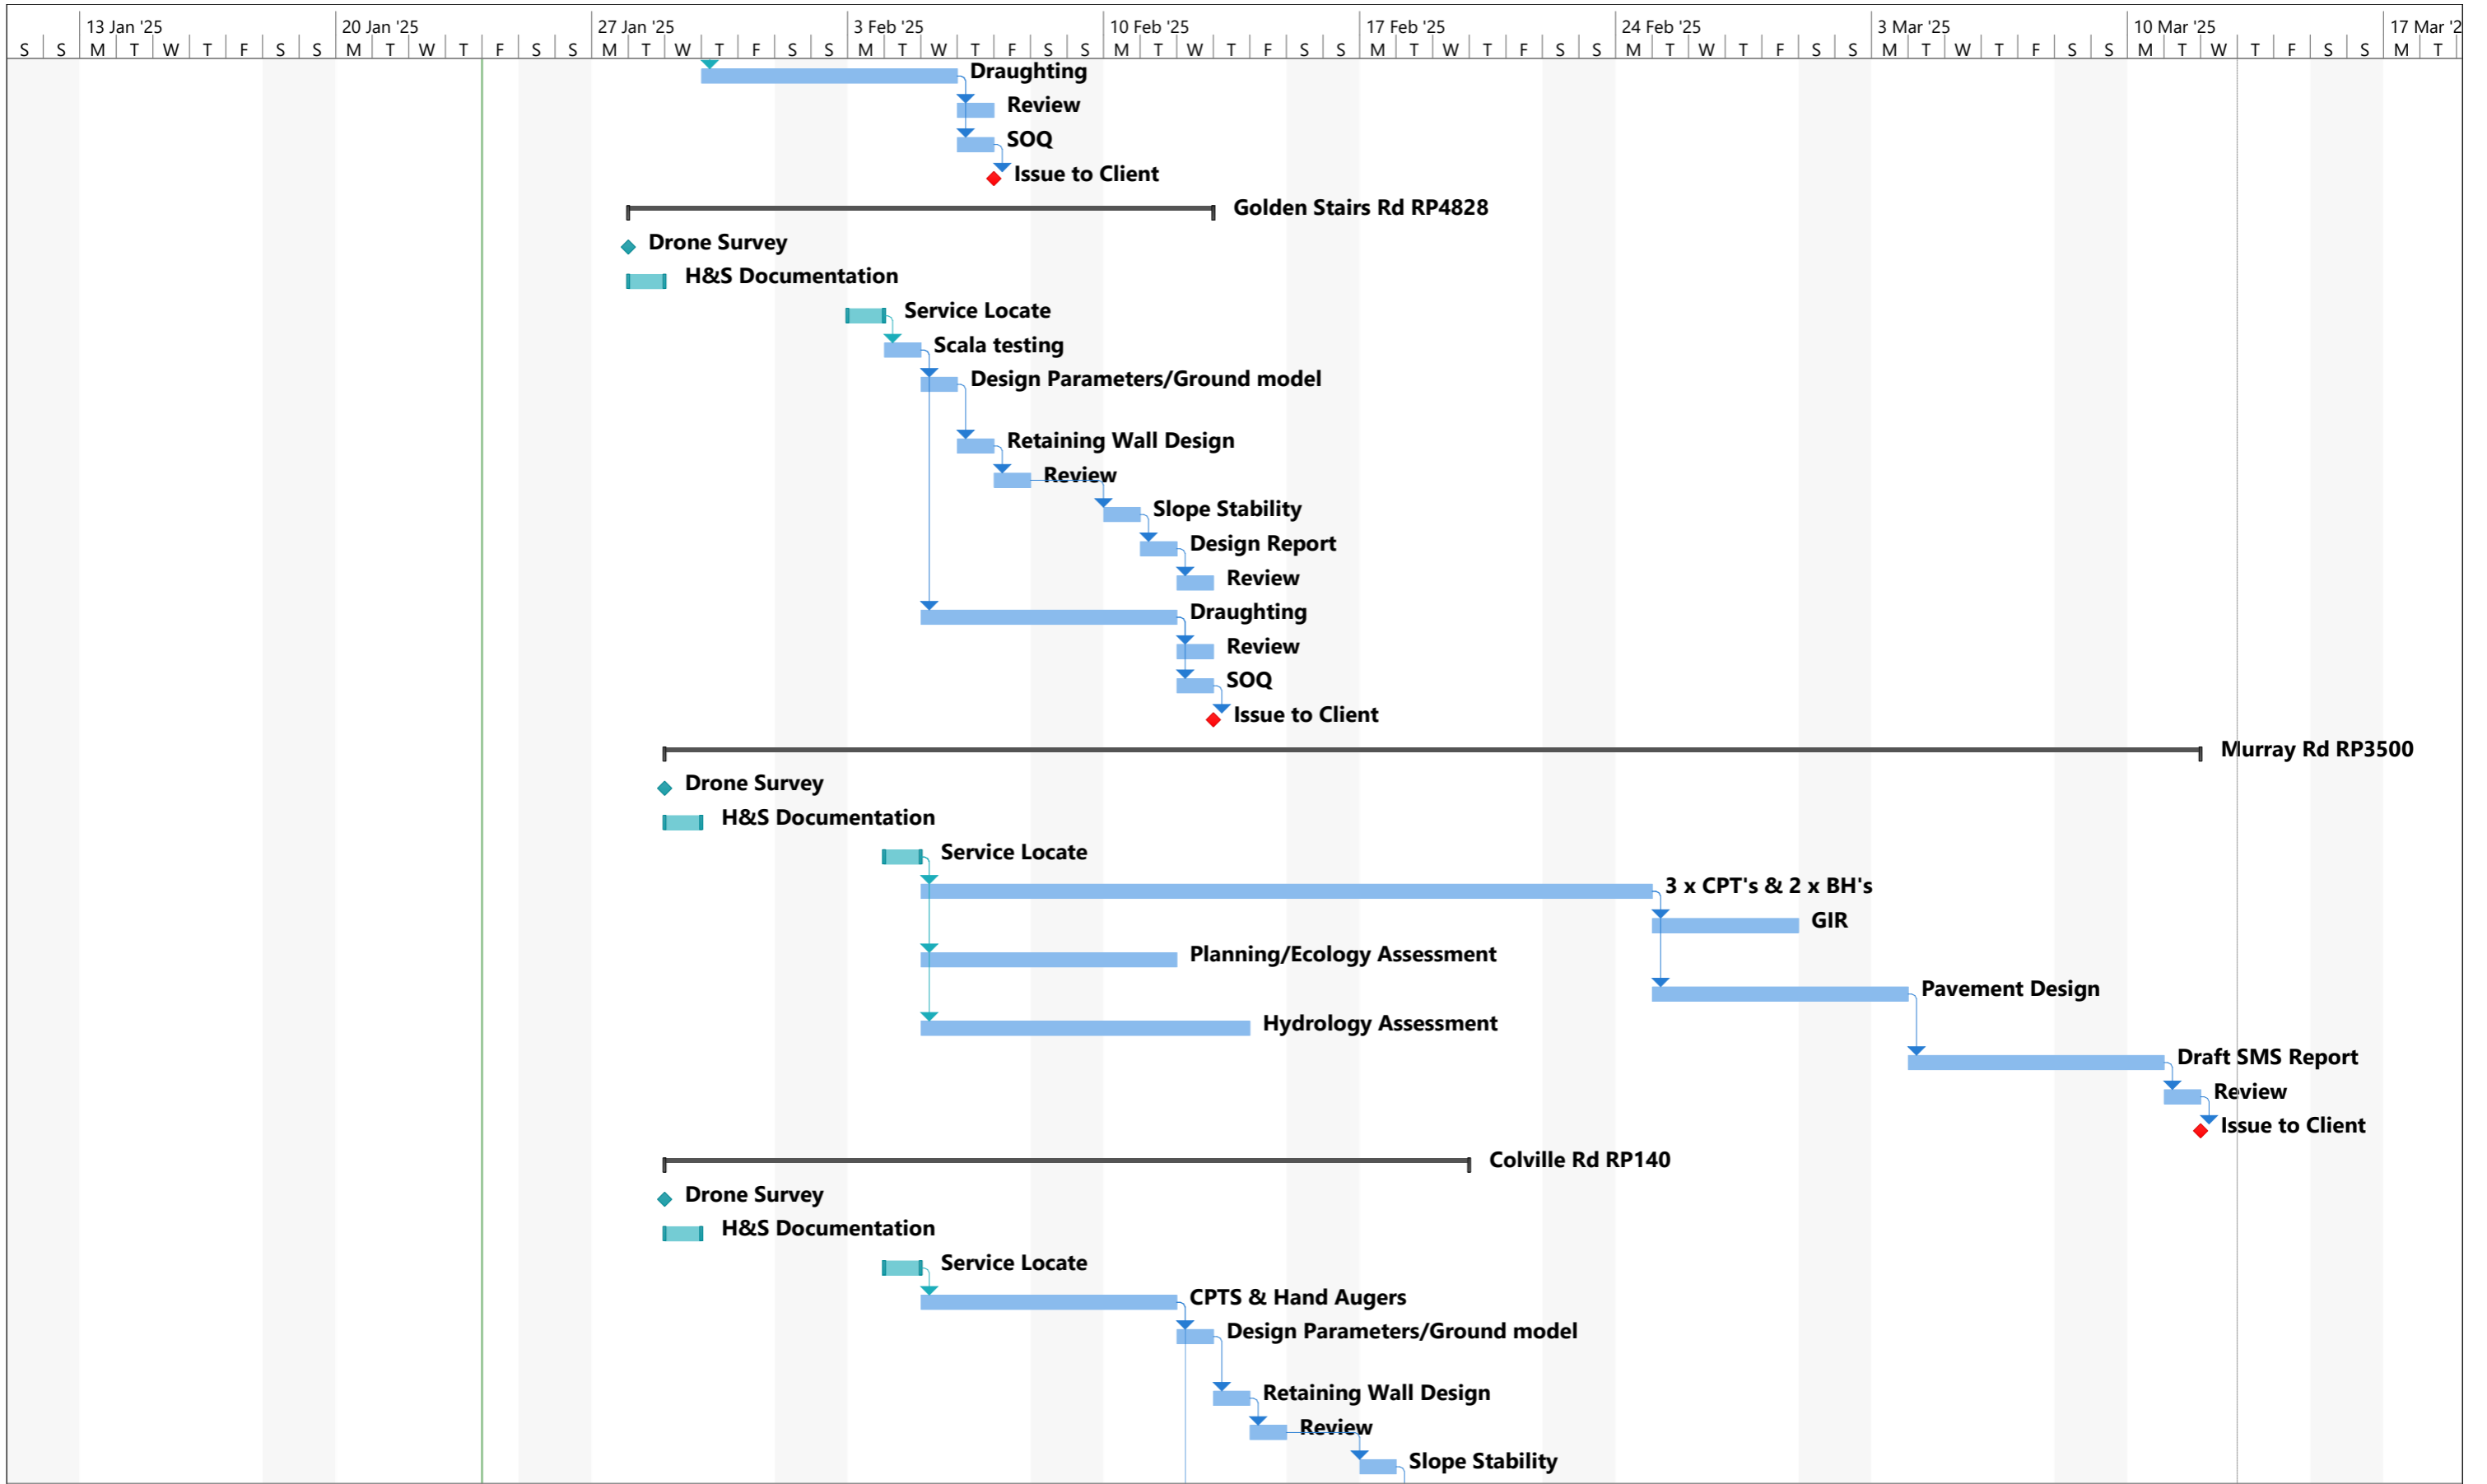

Project: KDC Programming  
Date: 24/01/25


Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			



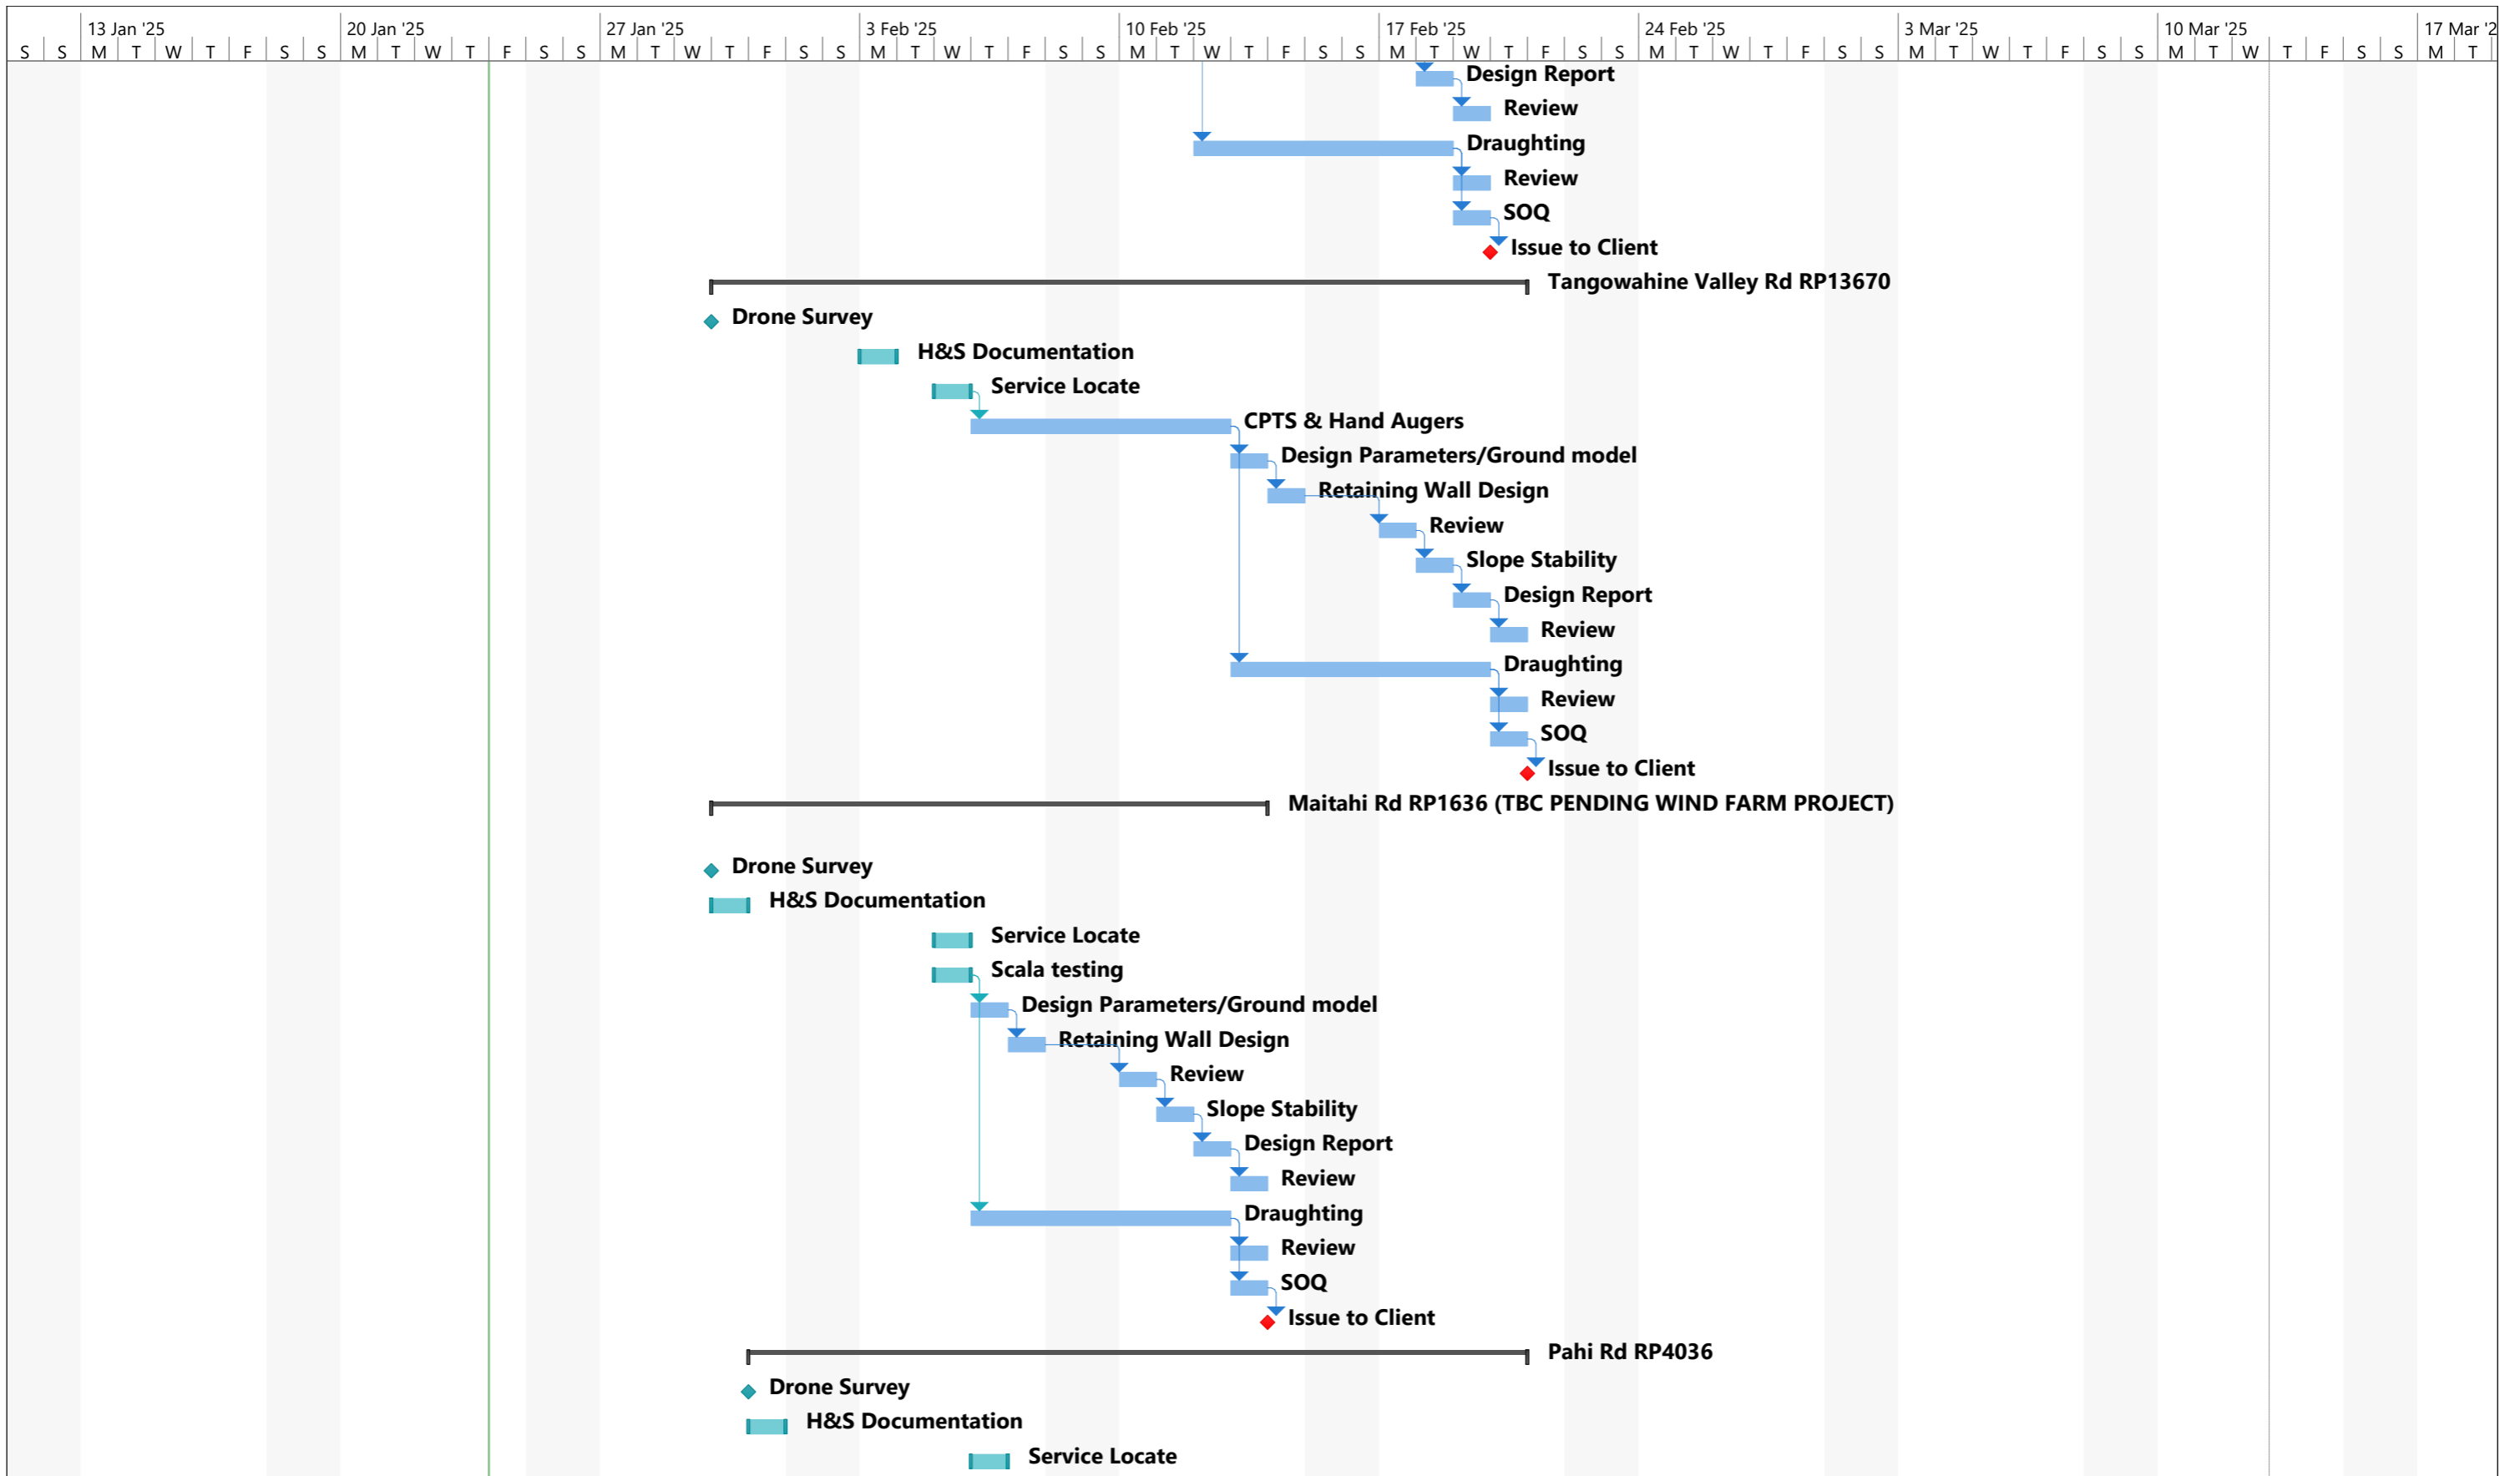


Project: KDC Programming  
Date: 24/01/25

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

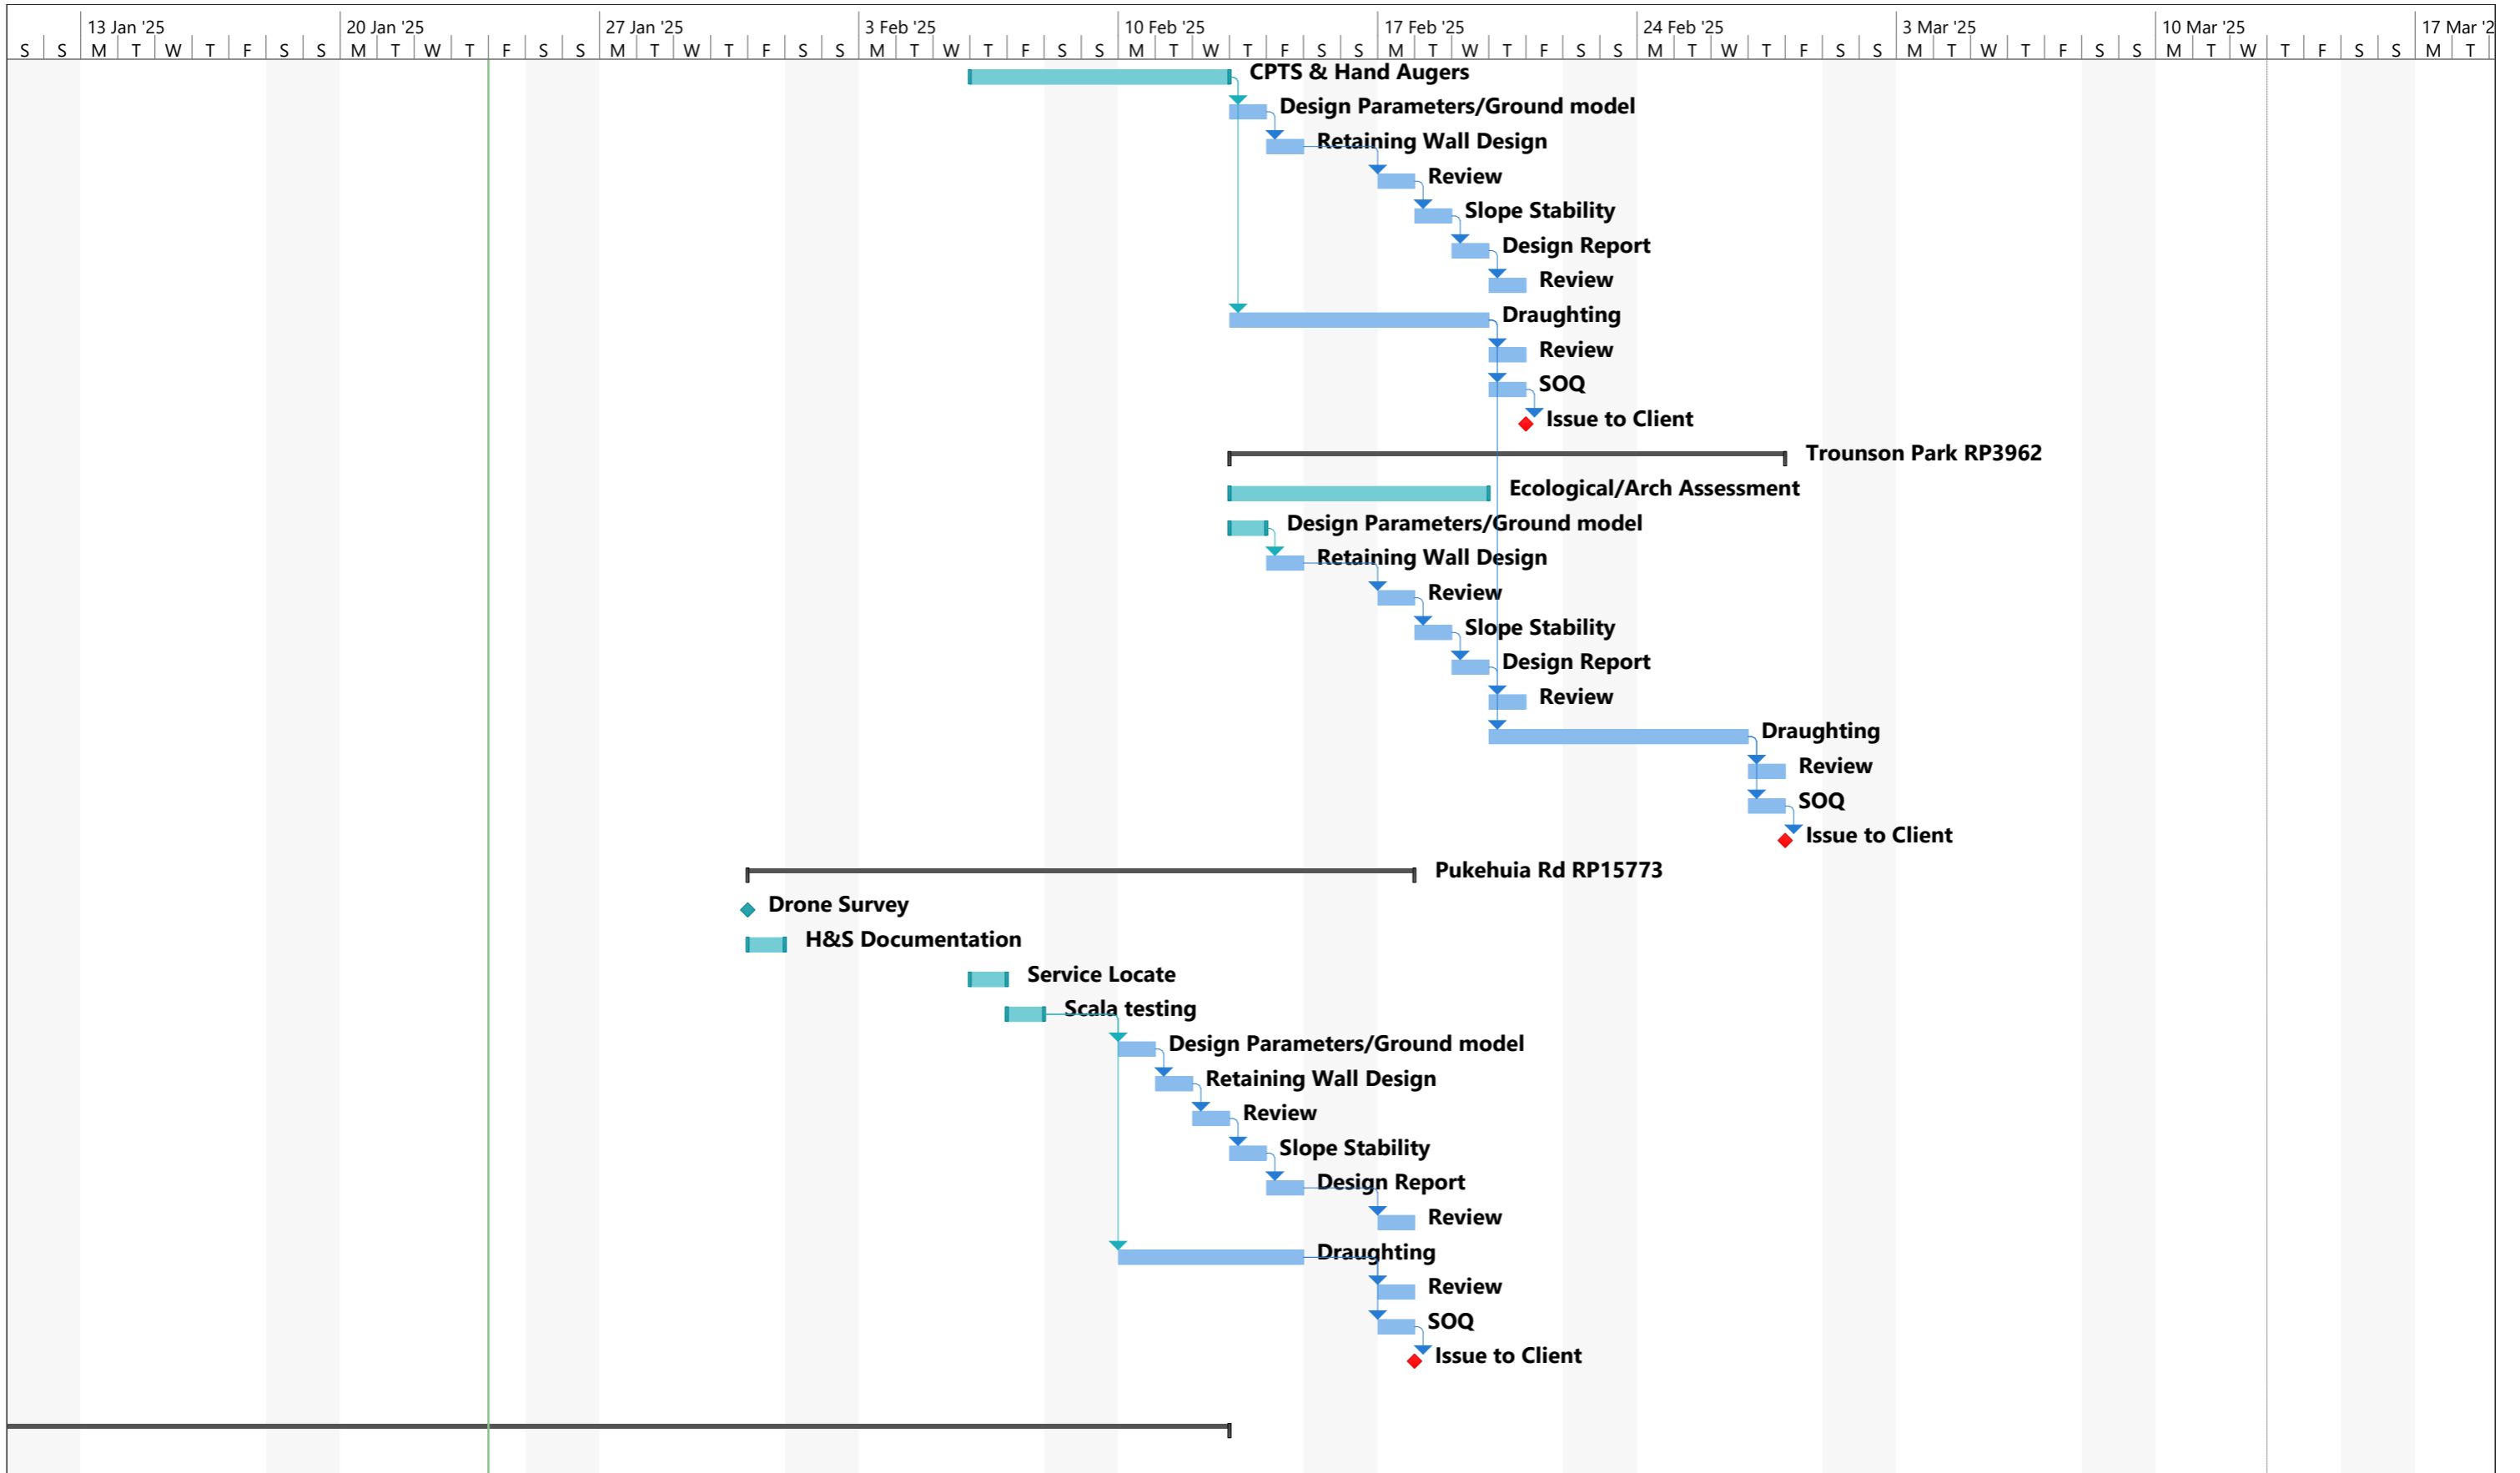

Project: KDC Programming  
Date: 24/01/25

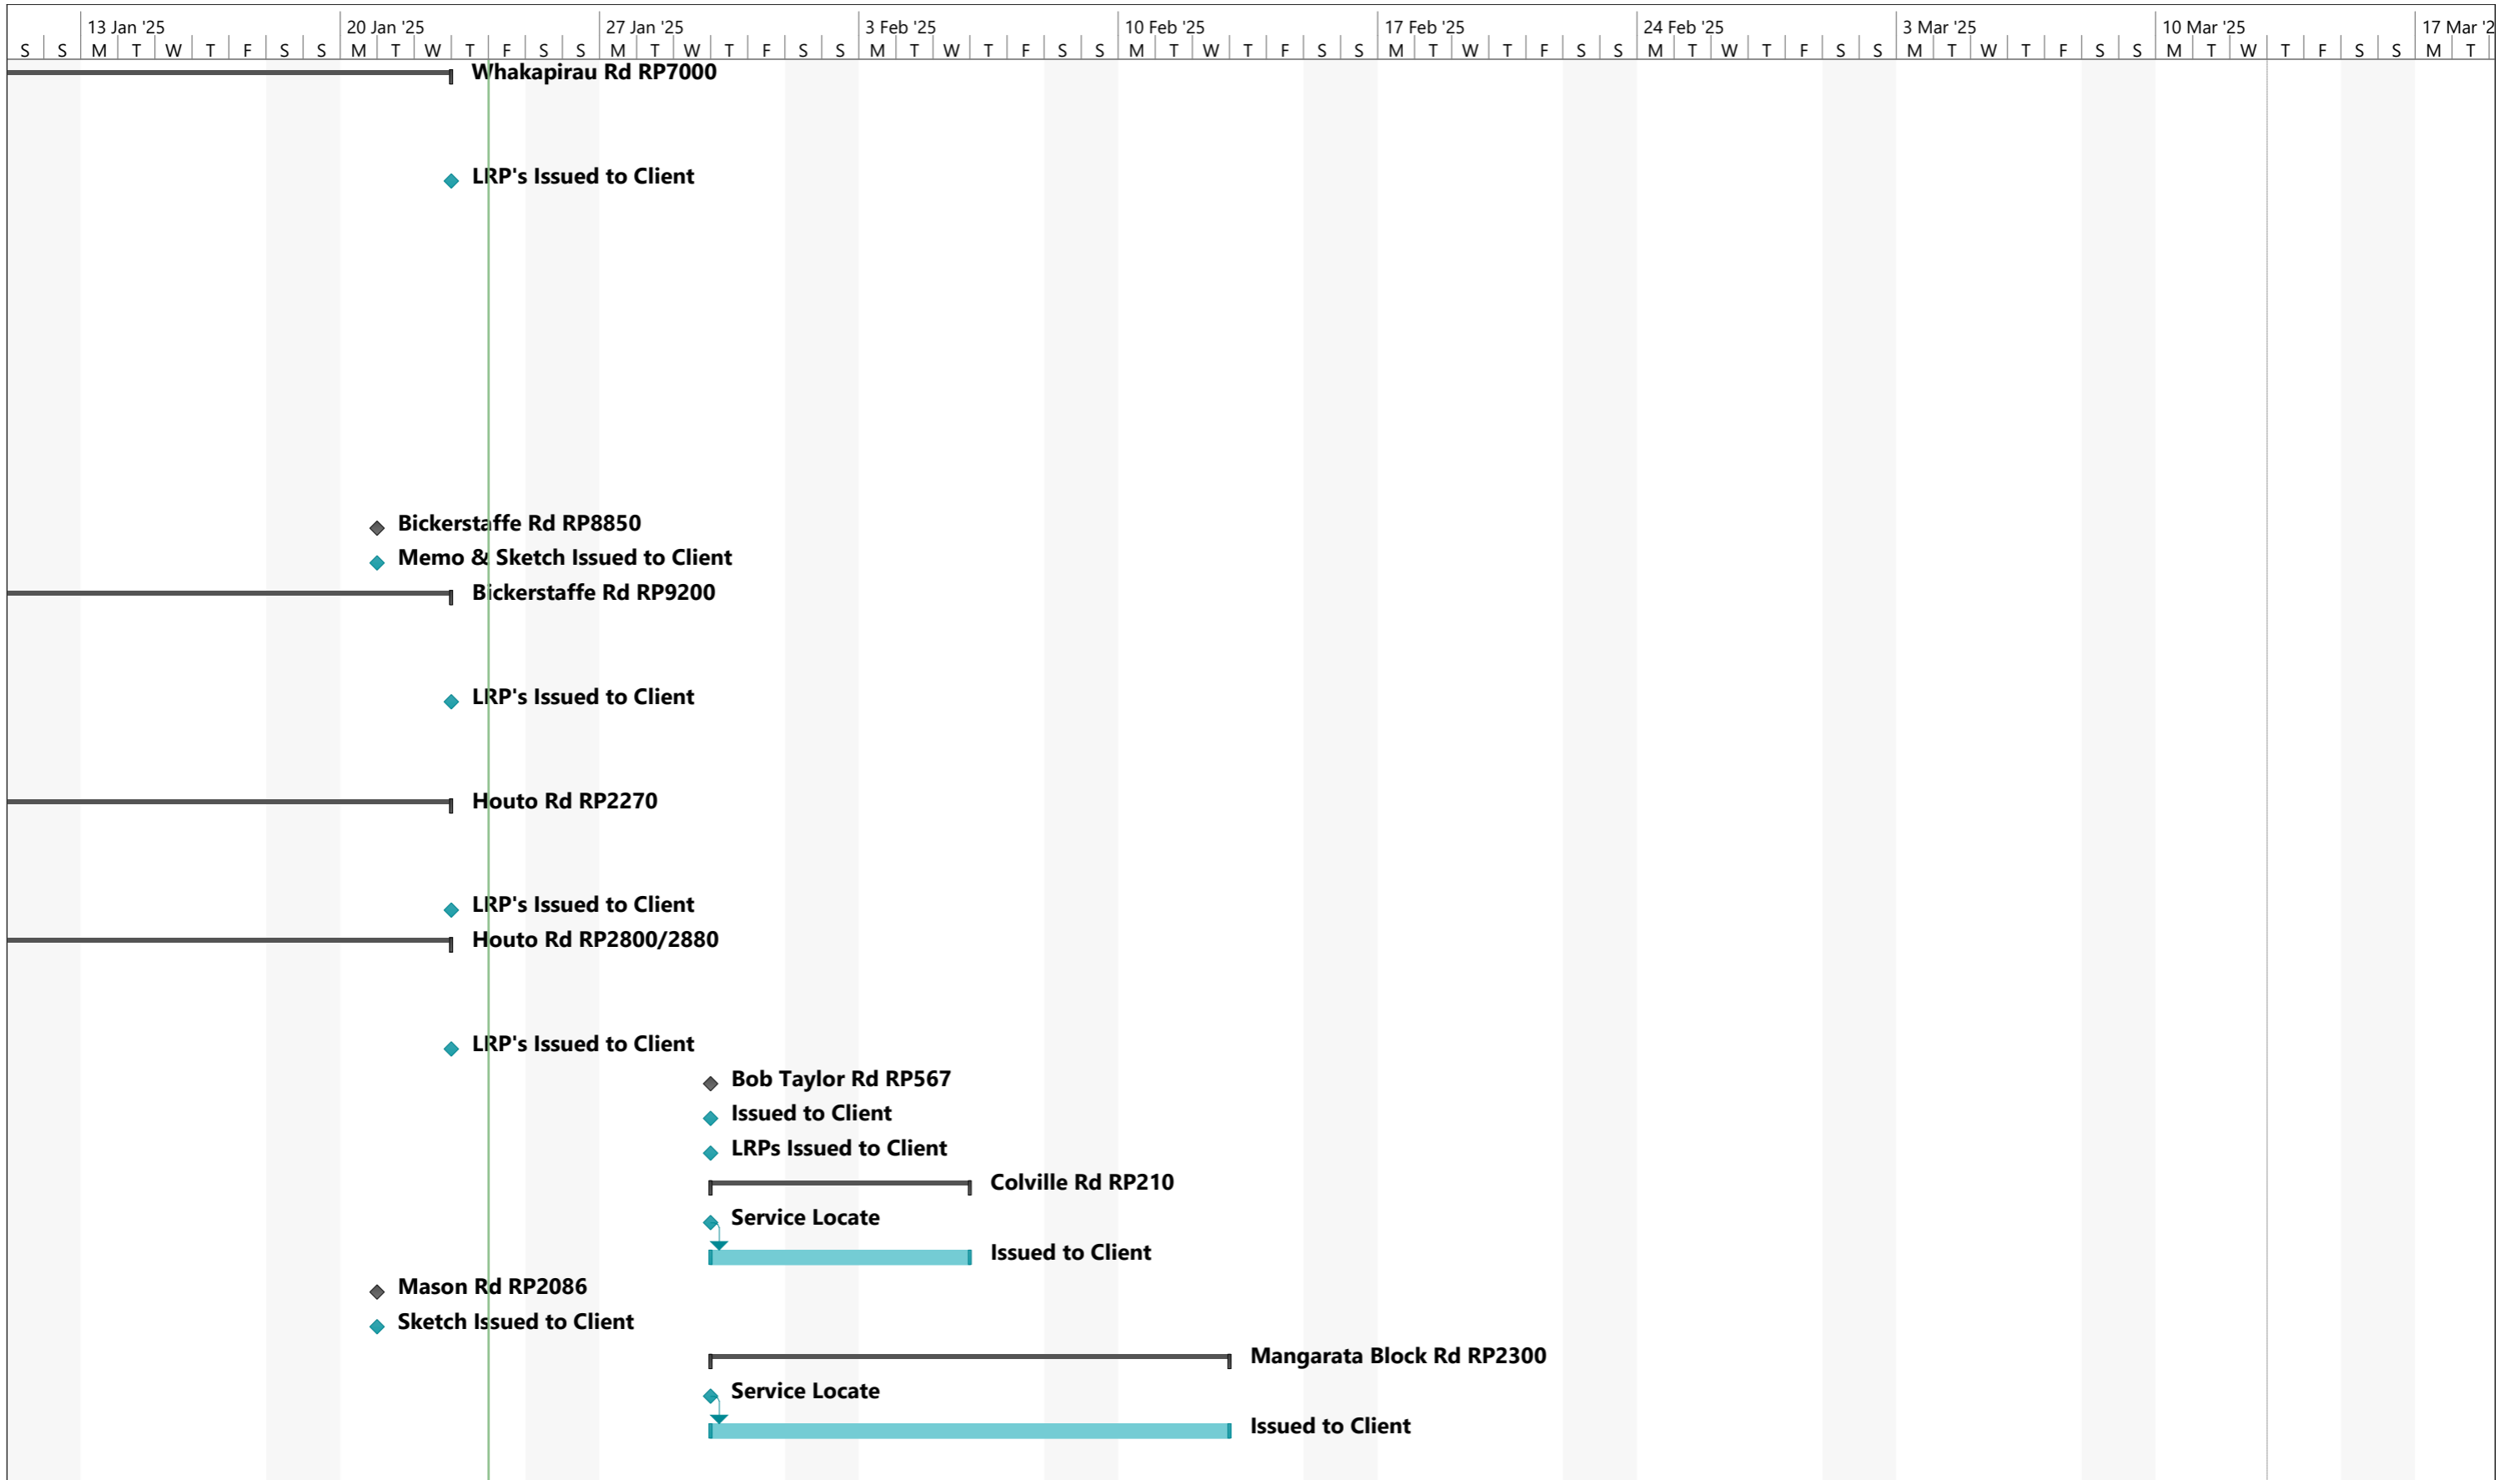

Project: KDC Programming Date: 24/01/25	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

S	S	13 Jan '25					S	S	20 Jan '25					F	S	S	27 Jan '25					M	T	W	T	F	S	S	3 Feb '25					M	T	W	T	F	S	S	10 Feb '25					M	T	W	T	F	S	S	17 Feb '25					M	T	W	T	F	S	S	24 Feb '25					M	T	W	T	F	S	S	3 Mar '25					M	T	W	T	F	S	S	10 Mar '25					M	T	W	T	F	S	S	17 Mar '25				
---	---	------------	--	--	--	--	---	---	------------	--	--	--	--	---	---	---	------------	--	--	--	--	---	---	---	---	---	---	---	-----------	--	--	--	--	---	---	---	---	---	---	---	------------	--	--	--	--	---	---	---	---	---	---	---	------------	--	--	--	--	---	---	---	---	---	---	---	------------	--	--	--	--	---	---	---	---	---	---	---	-----------	--	--	--	--	---	---	---	---	---	---	---	------------	--	--	--	--	---	---	---	---	---	---	---	------------	--	--	--	--



Project: KDC Programming Date: 24/01/25	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
